M. A. R. 57 (Rule 116) No. E 486832

Measurement Book

Serial No. .....

Name of work Drilling of borewells and providing pipeline at kempegowda garden, Nisarga layout and Saplagiri layout Surrounding area in ward No. 12 From ..... To .....

Name of Contractor of nature of Agency..... Sri Hanumantha G. Naik

Date of commencement of work... EE/DD/WO/10/2021-22 dt:- 27/05/2021

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Job code NO :- 012-20-00011 0						
	A.S NO :- EE/DD/AS/154/20-21/ Dated: 17/11/2020						
	T.S NO :- EE/DD/TS/38/20-21 Dated 17/11/2020						
	P code :- P 3293						
	Specification						

Scanned by CamScanner

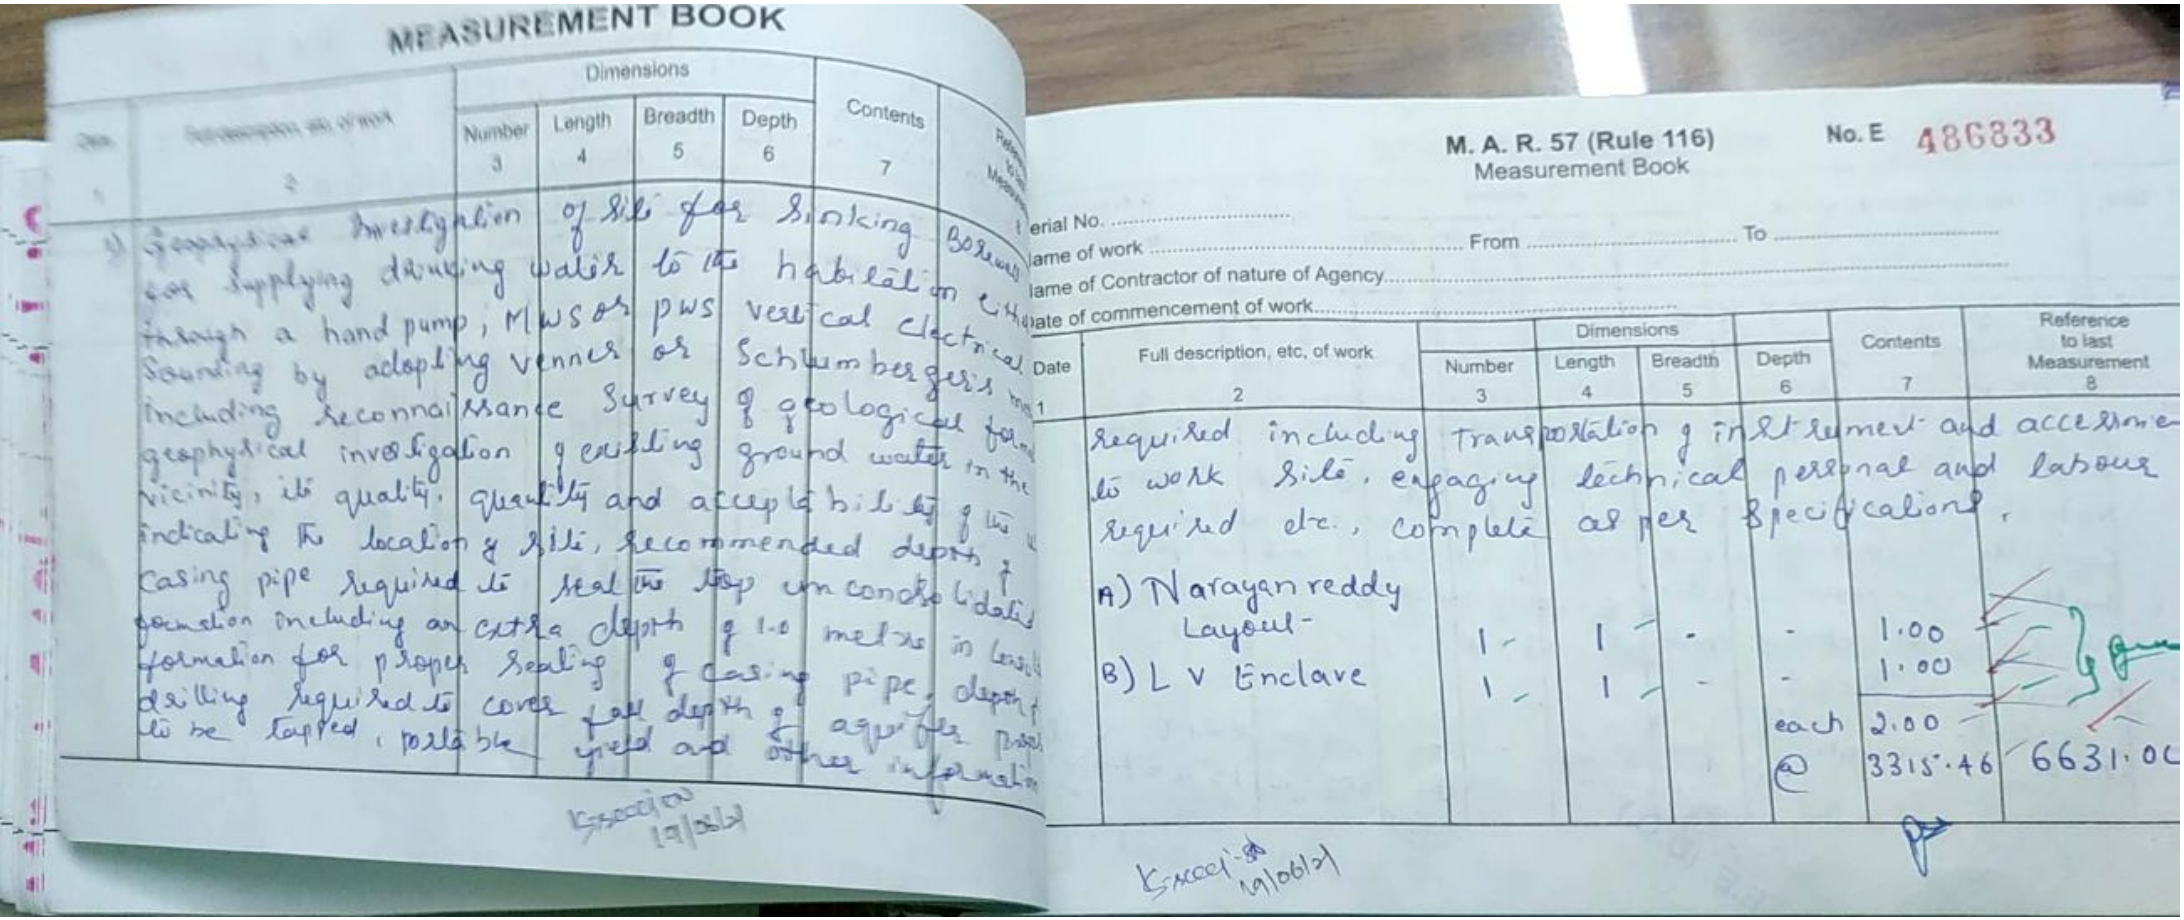

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	
	1) Geophysical Investigation of Site for Sinking Borewell for supplying drinking water to the habitation with through a hand pump, MWS or PWS vertical electrical Sounding by adopting Venner or Schlumberger's including reconnaissance survey of geological for geophysical investigation of existing ground water in the vicinity, its quality, quantity and acceptability of the indicating the location of site, recommended depth casing pipe required to seal the top unconsolidated formation including an extra depth of 1.0 metre in hard formation for proper sealing of casing pipe, depth drilling required to cover full depth of aquifer to be tapped, possible yield and other information required including Transportation of instrument and accessories to work site, engaging technical personal and labour required etc., complete as per Specifications.						
	A) Narayan reddy Layout-	1	1	-	-	1.00	
	B) L V Enclave	1	1	-	-	1.00	
					each	2.00	
					@	3315.46	6631.00

Executive Engineer 19/06/21

M. A. R. 57 (Rule 116) No. E 486833
Measurement Book

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

Executive Engineer 19/06/21

Scanned by CamScanner

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	2) Sinking of Borewell of 165 mm dia hydraulic rig of capacity 300 psig & above 1100 CMP & above in all strata including over burden. Fixing of casing pipes, collars & cap with necessary cutting, threading and welding including transportation of rig and supports vehicle, crew charges and cost of consumables etc complete including yield testing at the final depth with a minimum working & compressor for one hour as specified etc., complete as per Specification.						
	A) Narayana Reddy Layout.						
	1) 0.00 to 50.00 mts.	1	50.00	-	-	50.00 Rmt-r	
					@	305.33	15267

E.E. (D.D)

Kiseeri.SW 21/06/2021

M. A. R. 57 (Rule 116) No. E 486834
Measurement Book

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency.....
Date of commencement of work.....

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	3) 50.00 to 100.00 mtr		50.00	-	-	50.00 Rmt-r	
	4) 100.00 to 150.00 mtr	1	50.00	-	@	388.92	19446.00
						50.00 Rmt-r	
	5) 150.00 to 200.00 mtr	1	50.00	-	@	401.23	20062.00
						50.00 Rmt-r	
	6) 200.00 to 250.00 mtr	1	50.00	-	@	471.63	23582.00
						50.00 Rmt-r	
	7) 250.00 to 300.00 mtr	1	50.00	-	@	557.86	27893
						50.00 Rmtr	
					@	615.93	30797

E.E. (D.D)

Kiseeri.SW 21/06/2021

Scanned by CamScanner

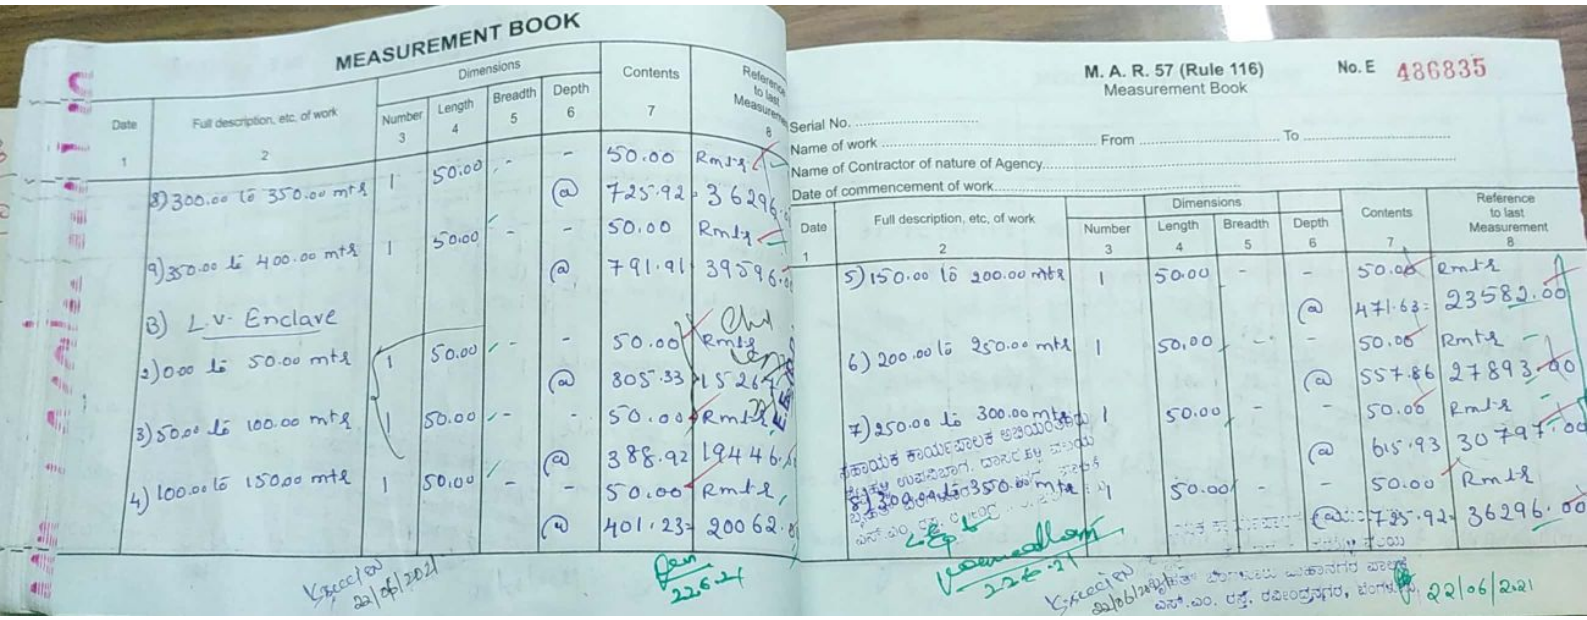

MEASUREMENT BOOK

Date	Full description, etc. of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	8) 300.00 to 350.00 mtr	1	50.00	-	-	50.00 Rmtr	
					@	725.92	36296.00
	9) 350.00 to 400.00 mtr	1	50.00	-	-	50.00 Rmtr	
					@	791.91	39596.00
	B) L.V. Enclave						
	2) 0.00 to 50.00 mtr	1	50.00	-	-	50.00 Rmtr	
					@	805.33	40266.00
	3) 50.00 to 100.00 mtr	1	50.00	-	-	50.00 Rmtr	
					@	388.92	19446.00
	4) 100.00 to 150.00 mtr	1	50.00	-	-	50.00 Rmtr	
					@	401.23	20062.00

Ksrec(w) 22/06/2021

Ram 22.6.21

M. A. R. 57 (Rule 116) No. E 486835
Measurement Book

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency.....
Date of commencement of work.....

Date	Full description, etc. of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	5) 150.00 to 200.00 mtr	1	50.00	-	-	50.00 Rmtr	
					@	471.63	23582.00
	6) 200.00 to 250.00 mtr	1	50.00	-	-	50.00 Rmtr	
					@	557.86	27893.00
	7) 250.00 to 300.00 mtr	1	50.00	-	-	50.00 Rmtr	
					@	615.93	30797.00
	8) 300.00 to 350.00 mtr	1	50.00	-	-	50.00 Rmtr	
					@	725.92	36296.00

Ksrec(w) 22/06/2021

22.6.21

22/06/2021

Scanned by CamScanner

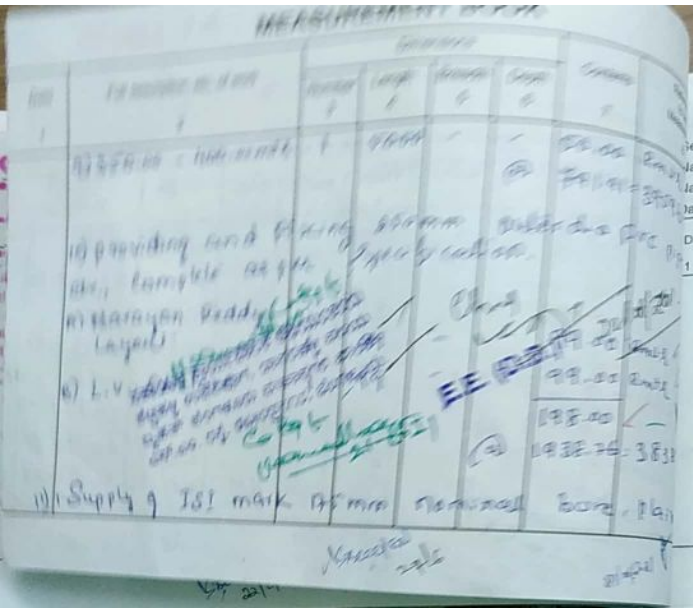

M. A. R. 57 (Rule 116)
Measurement Book

No. E 486836

Serial No. ..... From ..... To .....
Name of work .....
Name of Contractor of nature of Agency.....
Date of commencement of work.....

Date	Full description, etc, of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8
	Steel Casing pipe - grade of Steel PE-410 of wall thickness 5.4mm thick confirming to IS 4270: 2001 and latest amendment, electric resistance welded Steel tube material and confirming to IS 1387/1993 and manufactured by basic open hearth electric or basic oxygen process in random length of 5 to 7 mtrs. Both ends threaded confirming to IS 554/1985, one end bisced with Socket- confirming to IS 4270: 2001 and the other end with screwed pipes, All pipes shall be reasonably free from defects. The tubes shall be reasonably						

Scanned by CamScanner

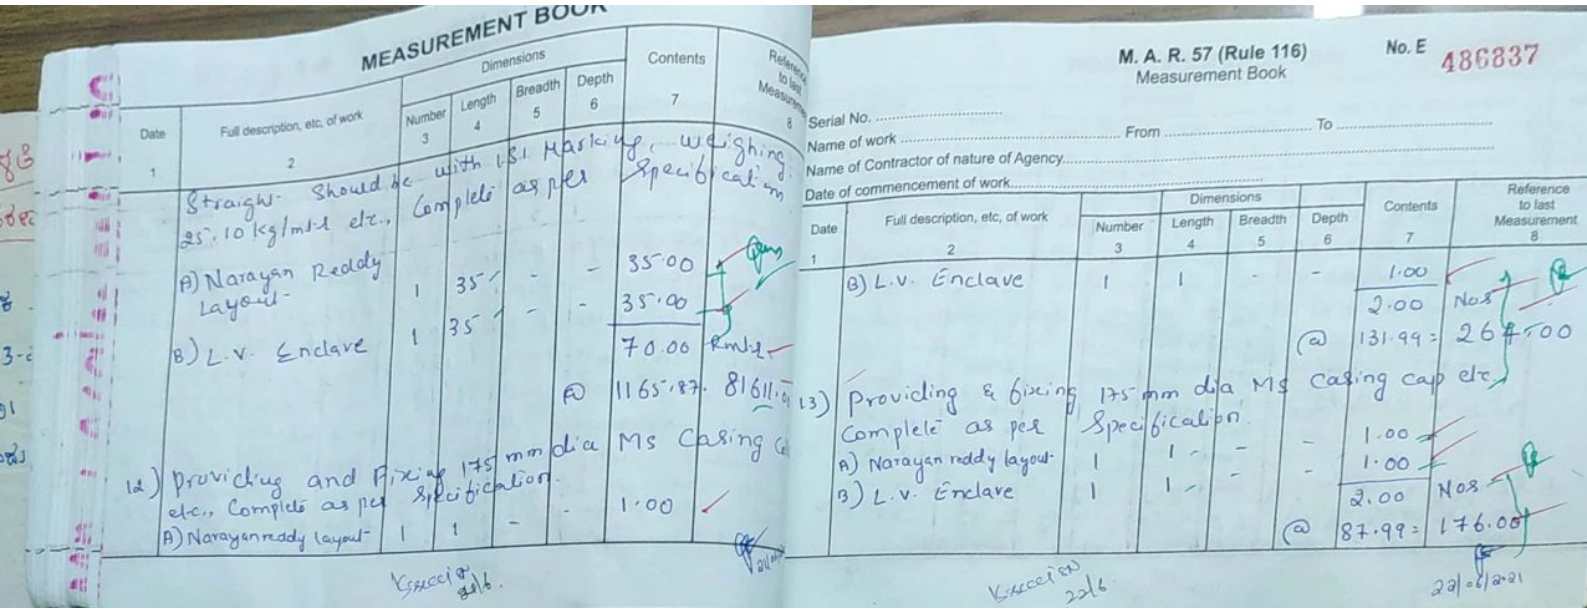

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	Straight Should be with I.S.I Marking, weighing 25.10 kg/m.t etc., Complete as per Specification						
	A) Narayan Reddy Layout-	1	35	-	-	35.00	
	B) L.V. Enclave	1	35	-	-	35.00	
						70.00 Rmtr	
					@	1165.87 = 81611.00	
	12) Providing and Fixing 175 mm dia MS Casing etc., Complete as per Specification.						
	A) Narayanreddy layout-	1	1	-	-	1.00	

Received 22/6.

M. A. R. 57 (Rule 116) No. E 486837
Measurement Book

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency.....
Date of commencement of work.....

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	B) L.V. Enclave	1	1	-	-	1.00	
						2.00 Nos	
					@	131.99 = 264.00	
	13) Providing & fixing 175 mm dia MS Casing cap etc., Complete as per Specification						
	A) Narayan reddy layout-	1	1	-	-	1.00	
	B) L.V. Enclave	1	1	-	-	1.00	
						2.00 Nos	
					@	87.99 = 176.00	

Received 22/6

22/06/2021

Scanned by CamScanner

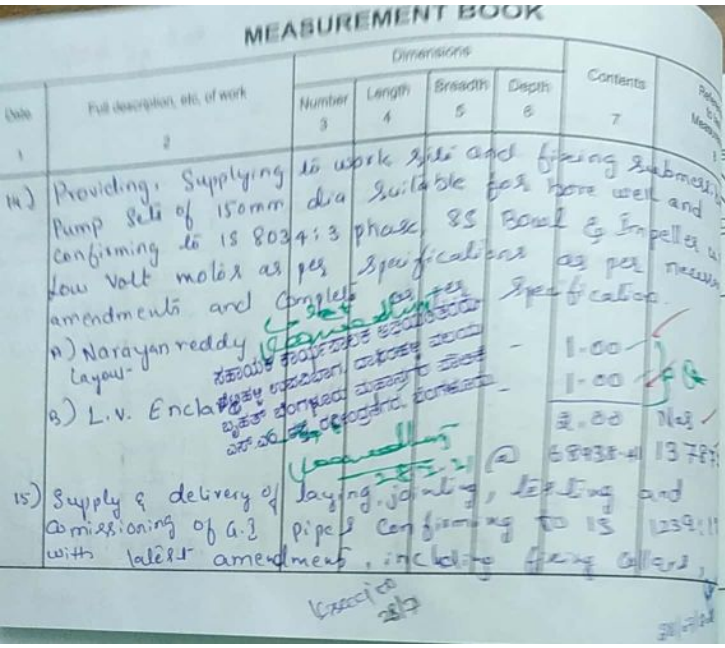

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	
14)	Providing, Supplying to work site and fixing Submersible Pump Sets of 150mm dia Suitable for bore well and confirming to IS 8034:3 phase, 85 Bowl & Impellers, Low Volt motors as per Specifications as per latest amendments and Complete as per Specifications.						
	A) Narayan reddy Layout- ನಾರಾಯಣ ರೆಡ್ಡಿ ಲೇಔಟ್					1.00	
	B) L.V. Enclave ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ ಎಸ್.ಎಂ. ಕೃಷ್ಣ ಲೇಔಟ್, ಬೆಂಗಳೂರು.					1.00	
						2.00	Nos
						68938.41	137876
15)	Supply & delivery of laying, jointing, testing and commissioning of G.I pipes Conforming to IS with latest amendments, including fixing collars,						1239.11

Executed 28/7

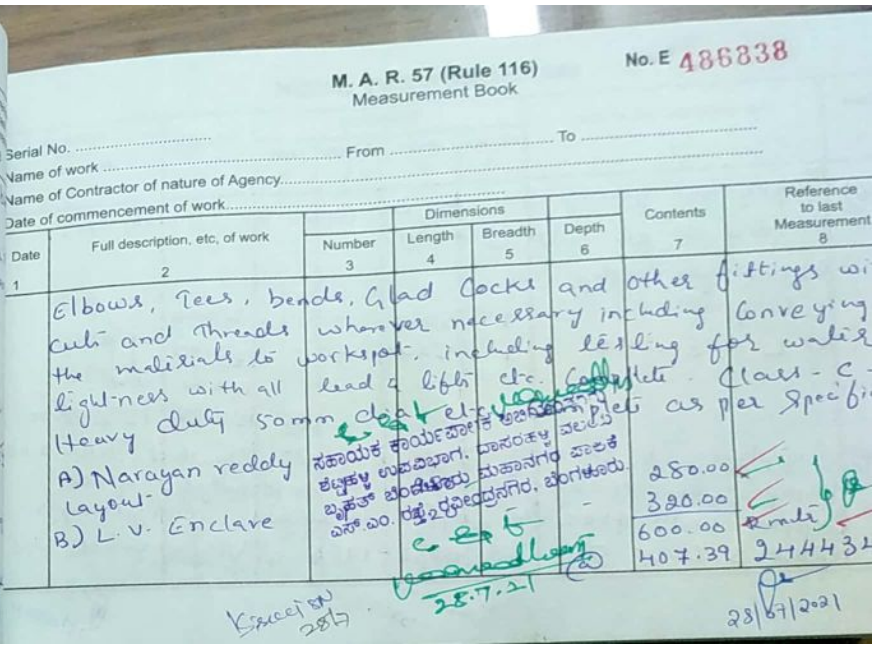

M. A. R. 57 (Rule 116)
Measurement Book

No. E 486338

Serial No. ..... From ..... To .....
Name of work .....
Name of Contractor of nature of Agency.....
Date of commencement of work.....

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	Elbows, Tees, bends, Gland Cocks and other fittings with cuts and Threads wherever necessary including Conveying the materials to worksite, including testing for water tightness with all lead & lifts etc. Complete Class - C Heavy duty 50mm dia etc. complete as per Specifications						
	A) Narayan reddy Layout- ನಾರಾಯಣ ರೆಡ್ಡಿ ಲೇಔಟ್					280.00	
	B) L.V. Enclave ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ ಎಸ್.ಎಂ. ಕೃಷ್ಣ ಲೇಔಟ್, ಬೆಂಗಳೂರು.					320.00	
						600.00	Rmts
						407.39	244434

28.7.21

Executed 28/7

28/07/2021

Scanned by CamScanner

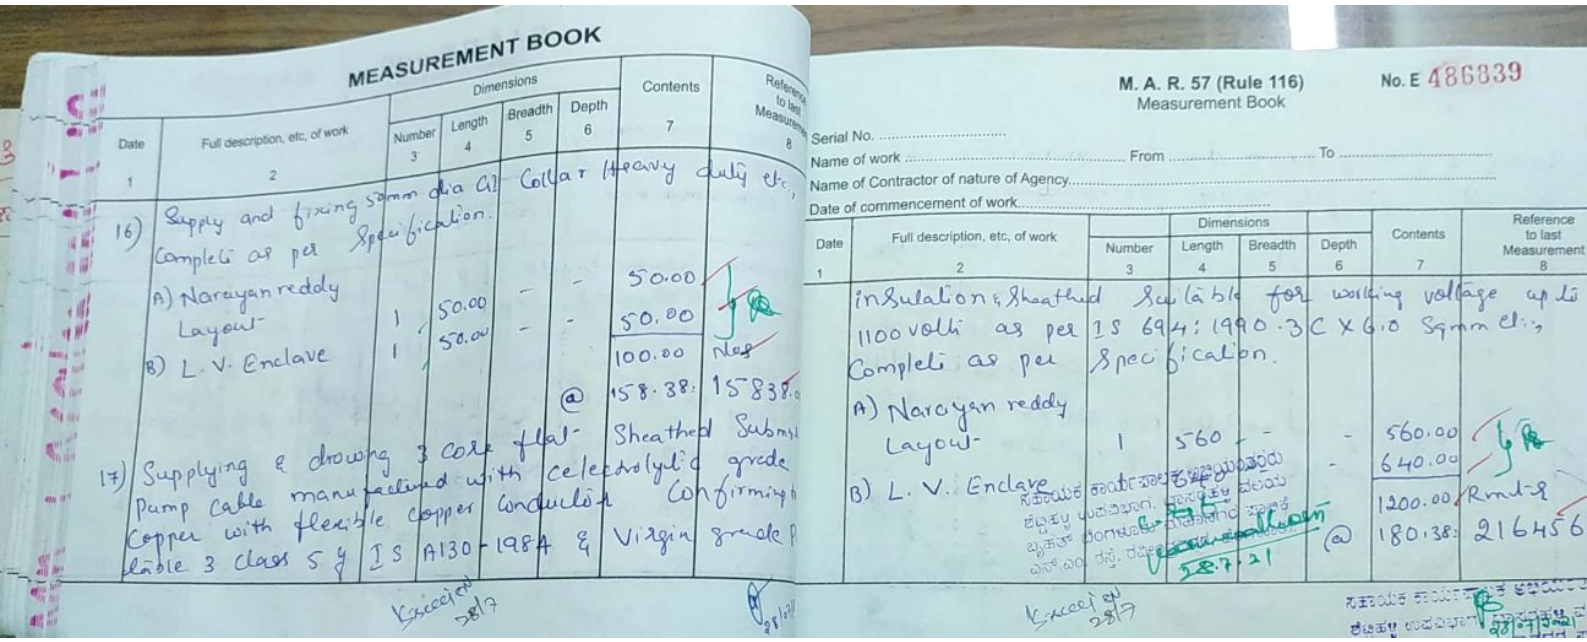

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	16) Supply and fixing 50mm dia CI Collar Heavy duty etc, Complete as per Specification.						
	A) Narayan reddy Layout-	1	50.00	-	-	50.00	
	B) L.V. Enclave	1	50.00	-	-	50.00	
						100.00	Nos
					@	158.38	15838.00
	17) Supplying & drawing 3 core flat Pump Cable manufactured with electrolytic grade Copper with flexible copper conductor Confirming to IS 4130-1984 & Virgin grade P						Sheathed Submsl

Succeed 28/7

M. A. R. 57 (Rule 116) No. E 486839
Measurement Book

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency.....
Date of commencement of work.....

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	insulation & Sheathed Suitable for working voltage upto 1100 volts as per IS 694:1990. 3C X 6.0 Sqmm Cu, Complete as per Specification.						
	A) Narayan reddy Layout-	1	560	-	-	560.00	
	B) L.V. Enclave				-	640.00	
						1200.00	Rmt-s
					@	180.38	216456

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಚೆಟ್ಟಿಹಳ್ಳಿ ಉಪವಿಭಾಗ, ಚಳ್ಳಕೆರೆ ವಲಯ
ಬೆಸ್ಕಾಂ ಬೆಂಗಳೂರು ನಗರ ಜಿಲ್ಲಾ
ಎಸ್.ಎಂ. ರಸ್ತೆ, ರಾಜಾಜಿನಗರ, ಬೆಂಗಳೂರು-560 010
28.7.21

Succeed 28/7

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಚೆಟ್ಟಿಹಳ್ಳಿ ಉಪವಿಭಾಗ

Scanned by CamScanner

18) Supply & fixing 50mm dia GI union with ISI mark etc., Complete as per Specification.

1	1	-	-	1.00
1	1	-	-	1.00
				2.00 Nos

@ 196.83 : 394.00

19) Supply & fixing 50mm dia G.I Nipple with ISI mark etc., Complete as per Specification.

1	3	-	-	3.00
1	3	-	-	3.00
				6.00 Nos

@ 91.77 : 551.00

Kseela 28/7

M. A. R. 57 (Rule 116)
Measurement Book

No. E 486840

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency .....
Date of commencement of work .....

Date	Full description, etc, of work	Number	Dimensions: Length	Dimensions: Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	20) Supply & delivery at site of brand new best make non-return valve as per IS 778/1984 with ISI mark as per its latest amendments 50 mm dia etc., Complete as per Specification.	1	1	-	-	1.00	
		1	1	-	-	1.00	
						2.00 Nos	
					@	1033.85	2068.00
	21) Supplying & fixing 50 mm dia GI elbow with IS						

Kseela 28/7

28/07/20

Scanned by CamScanner

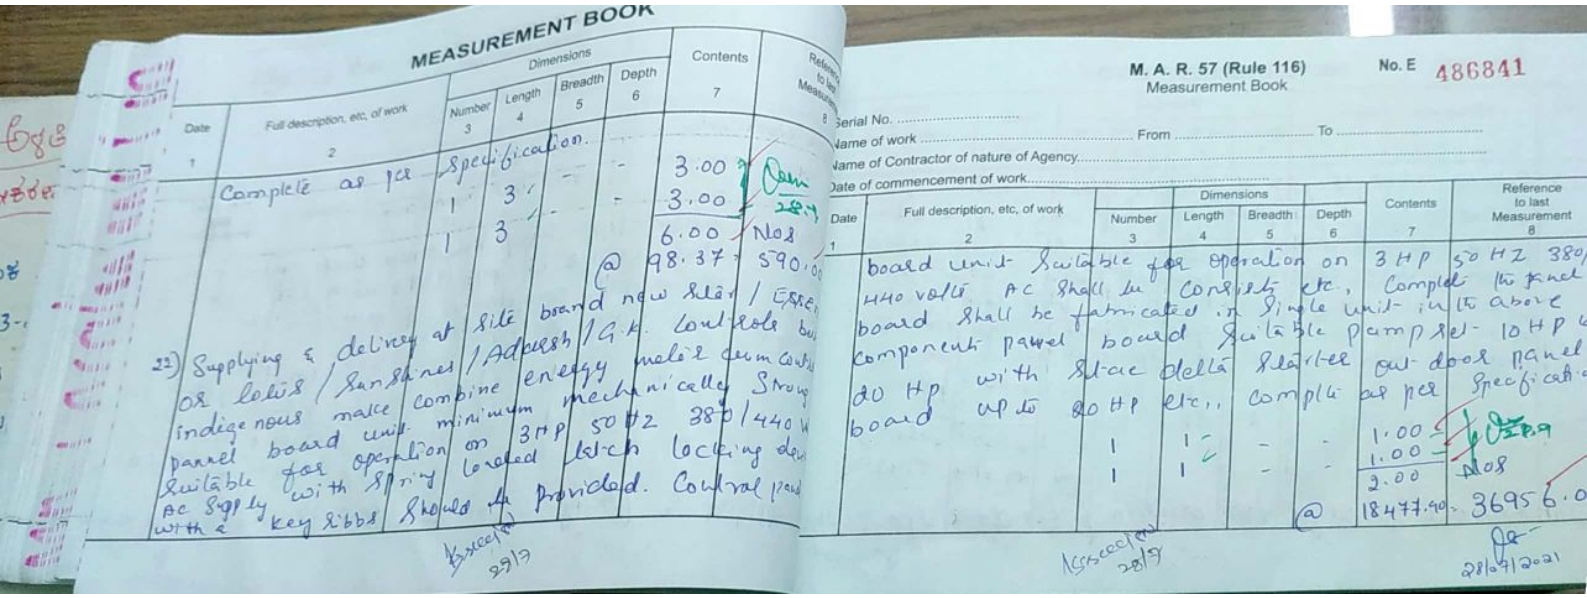

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	Complete as per Specification.	-	-	-		3.00	
		1	3	-	-	3.00	
		1	3	-	-	6.00 Nos @ 98.37 = 590.0	
22)	Supplying & delivery at site board new Siemens / Essen / Or Legris / Sunshines / Adpush / G.K. Control Gear indigenous make combine energy make dem control panel board unit minimum mechanically Strong Suitable for operation on 3HP 50 HZ 380/440 V AC Supply with Spring loaded latch locking device with 2 key ribbs should be provided. Control panel						

Accepted 28/9

M. A. R. 57 (Rule 116)
Measurement Book

No. E 486841

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency.....
Date of commencement of work.....

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	board unit Suitable for operation on 440 volts AC Shall be Consist etc., Complete panel board Shall be fabricated in Single unit in its above component panel board Suitable pump set- 10 HP to 20 HP with Star delta Starter board upto 20 HP etc., complete as per Specification					3 HP 50 HZ 380/ Complete panel out-door panel as per Specification	
		1	1	-	-	1.00	
		1	1	-	-	1.00	
						2.00 Nos	
					@	18477.90 = 3695 6.0	

Accepted 28/9

28/09/2021

Scanned by CamScanner

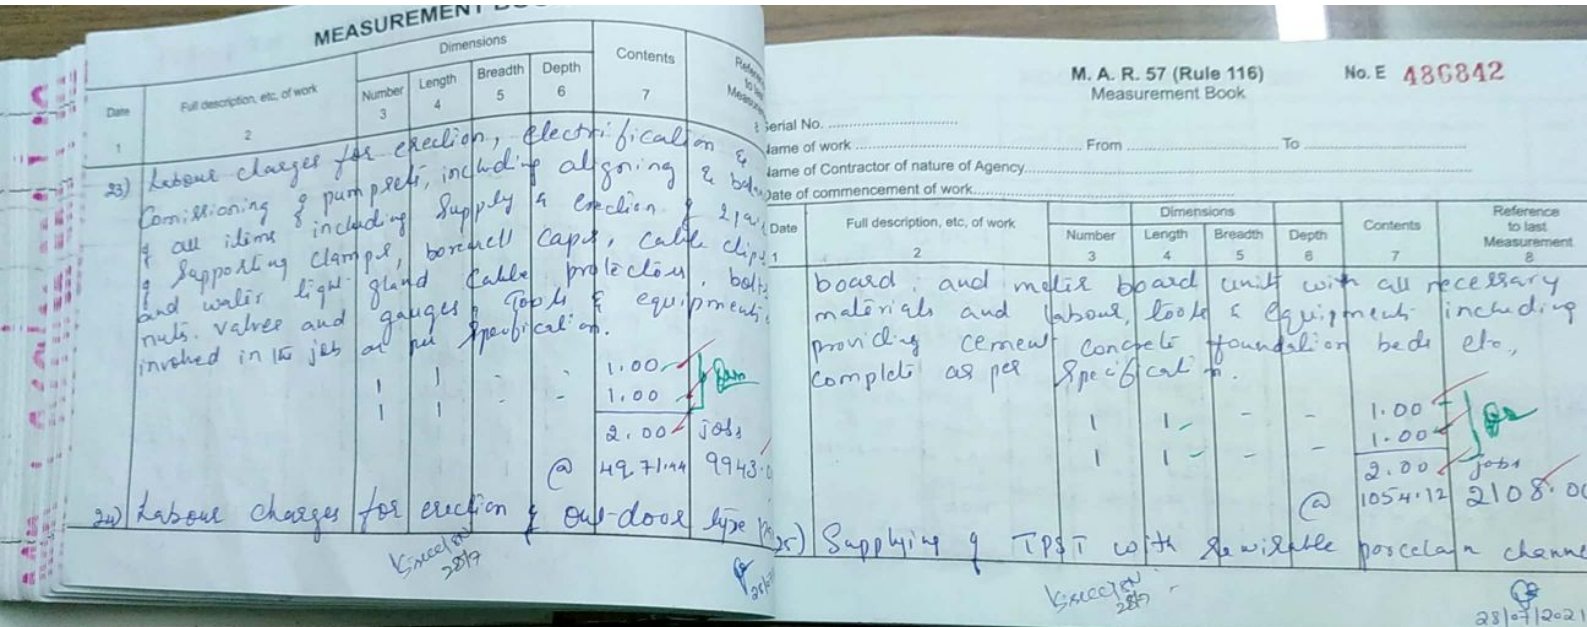

MEASUREMENT

Date	Full description, etc., of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
23)	Labour charges for erection, electrification & Comissioning of pumpsets, including aligning & balancing of all items including Supply & erection of 2 nos Supporting clamps, borewell caps, cable clips and water light gland cable protections, bolts nuts, valves and gauges, Tools & equipments involved in the job as per specification.	1	1	-	-	1.00	
		1	1	-	-	1.00	
						2.00 jobs	
					@	4971.44	9943.00
24)	Labour charges for erection & Out-door type (25)						

Executive Engr

M. A. R. 57 (Rule 116) No. E 486842
Measurement Book

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency.....
Date of commencement of work.....

Date	Full description, etc., of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	board, and meter board unit with all necessary materials and labour, tools & equipments including providing cement concrete foundation beds etc, complete as per Specification.	1	1	-	-	1.00	
		1	1	-	-	1.00	
						2.00 jobs	
					@	1054.12	2108.00
25)	Supplying & TPST with serviceable porcelain channe						

Executive Engr

28/07/2021

Scanned by CamScanner

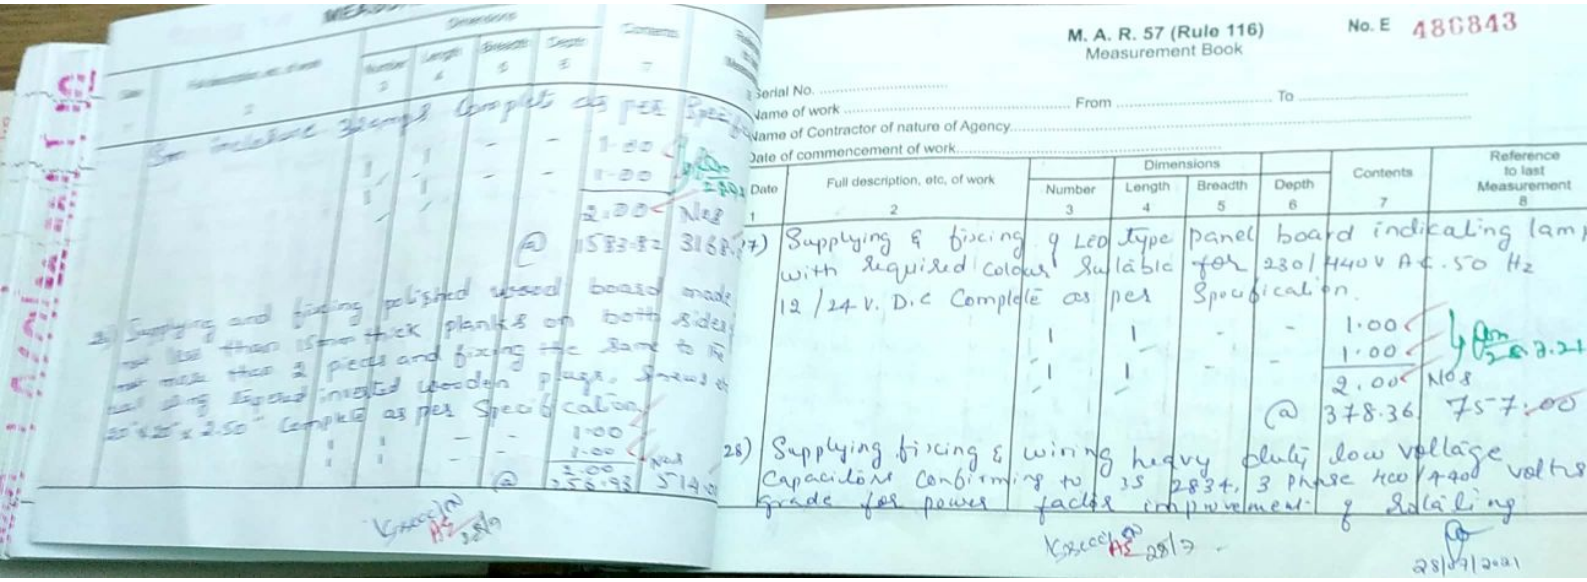

M. A. R. 57 (Rule 116)
Measurement Book

No. E 486843

Serial No. .....
Name of work ..... From ..... To .....
Name of Contractor of nature of Agency.....
Date of commencement of work.....

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	Supplying & fixing 9 LED type panel board indicating lamp with required colour Suitable for 230/440 V A.C. 50 Hz 12/24 V. D.C Complete as per Specification.	1	1	-	-	1.00	
		1	1	-	-	1.00	
		1	1	-	-	2.00 Nos	
					@	378.36	757.00
	Supplying fixing & wiring heavy duty low voltage Capacitor Confirming to IS 2834, 3 phase 440/440 volts grade for power factor improvement & Isolating						

28/9/2021

MEASU...

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	machineries like induction motor 2 KVAR Complete as per the direction & Engineer incharge.	1	1	–	–	1.00	
		1	1	–	–	1.00	
		1	1			2.00 Nos	
					@	35196	704.00
29)	Supplying & fixing miniature circuit breakers on existing materials and c type curve, indicators energy Cords-3 with short circuit breaking Capa & 10k & Complete wiring as required Conforming to 60898 6 to 32 amps complete as per Specification.	1	1	–	–	1.00	
		1	1	–	–	1.00	
		1	1			2.00 Nos	
					@	1509.03	3018.06

Verified 28/7

28/07/2017

M. A. R. 57 (Rule 116)
Measurement Book

No. E 486844

Serial No. .....

Name of work ..... From ..... To .....

Name of Contractor of nature of Agency.....

Date of commencement of work.....

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
30)	Supplying & fixing wiring earth electrode for grounding Conduits Ic cubicles & their equipments on the meter boards using 40mm dia 2.90mm thick GI pipe 2.5 mts long burried in a pit. The pit shall be filled with equal proportions of salt & charcoal 150mm all around the pipe to complete depth the Connection from pipe to the Conduits etc., is to be established through GI wire of size as per ISI Specification 7.3.3 & IS 732 upto 12mm dia bolts, nuts, washers, check nuts, etc., the pipe shall have						

Verified 28/7

Scanned by CamScanner

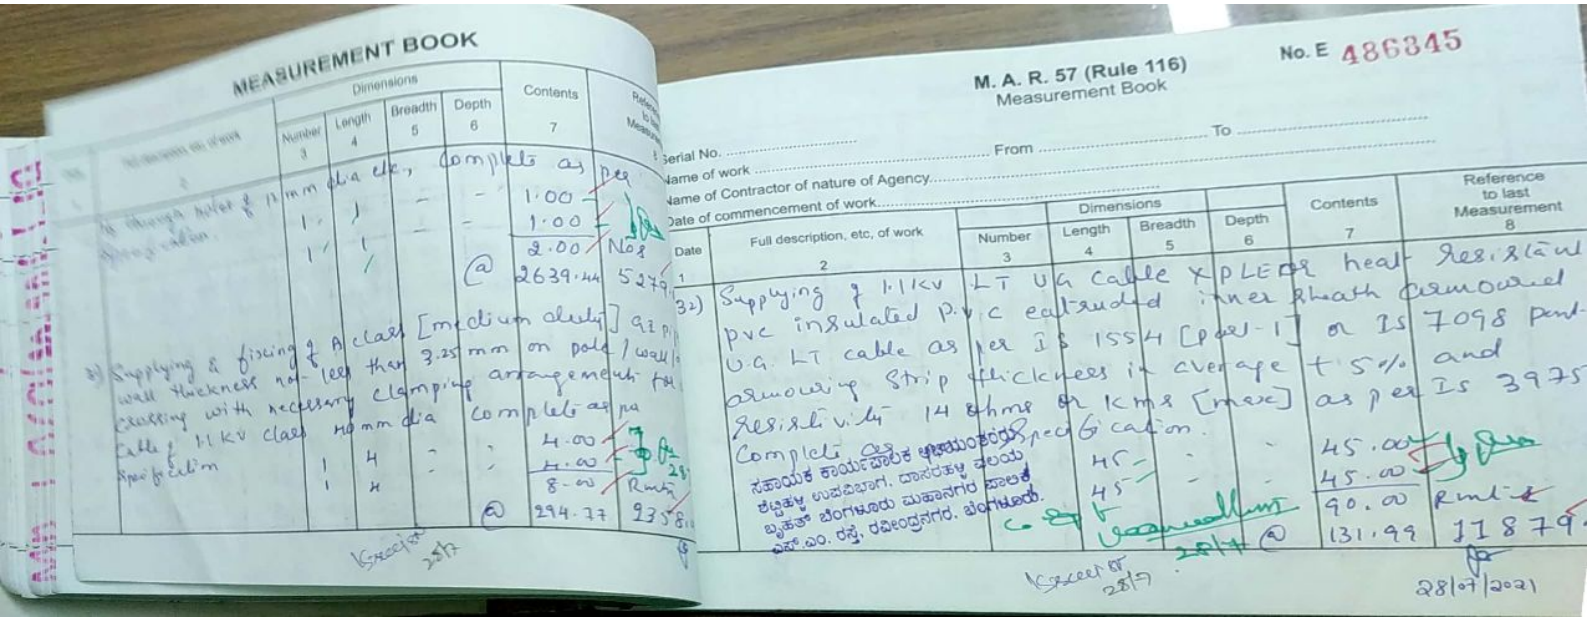

MEASUREMENT BOOK

Number	Length	Breadth	Depth	Contents	Reference to last Measurement
3	4	5	6	7	
				1.00	
1	1	-	-	1.00	
1	1	-	-	2.00	Nos
			@	2639.44	5279

M. A. R. 57 (Rule 116)
Measurement Book

No. E 486845

Serial No. ..... From ..... To .....
Name of work .....
Name of Contractor of nature of Agency.....
Date of commencement of work.....

Date	Full description, etc, of work	Number	Dimensions Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	32) Supplying & 1.1 kv LT UG Cable XPLE or heat Resisting PVC insulated PVC coated inner sheath armoured UG LT cable as per IS 1554 [Part-1] or IS 7098 Part-I removing Strip thickness in average Resistivity 14 ohms or kms [more] as per IS 3975 Complete as per Specification.						
			45	-	-	45.00	
			45	-	-	45.00	
						90.00	Rmt
				@		131.99	11879

28/07/2021

Scanned by CamScanner

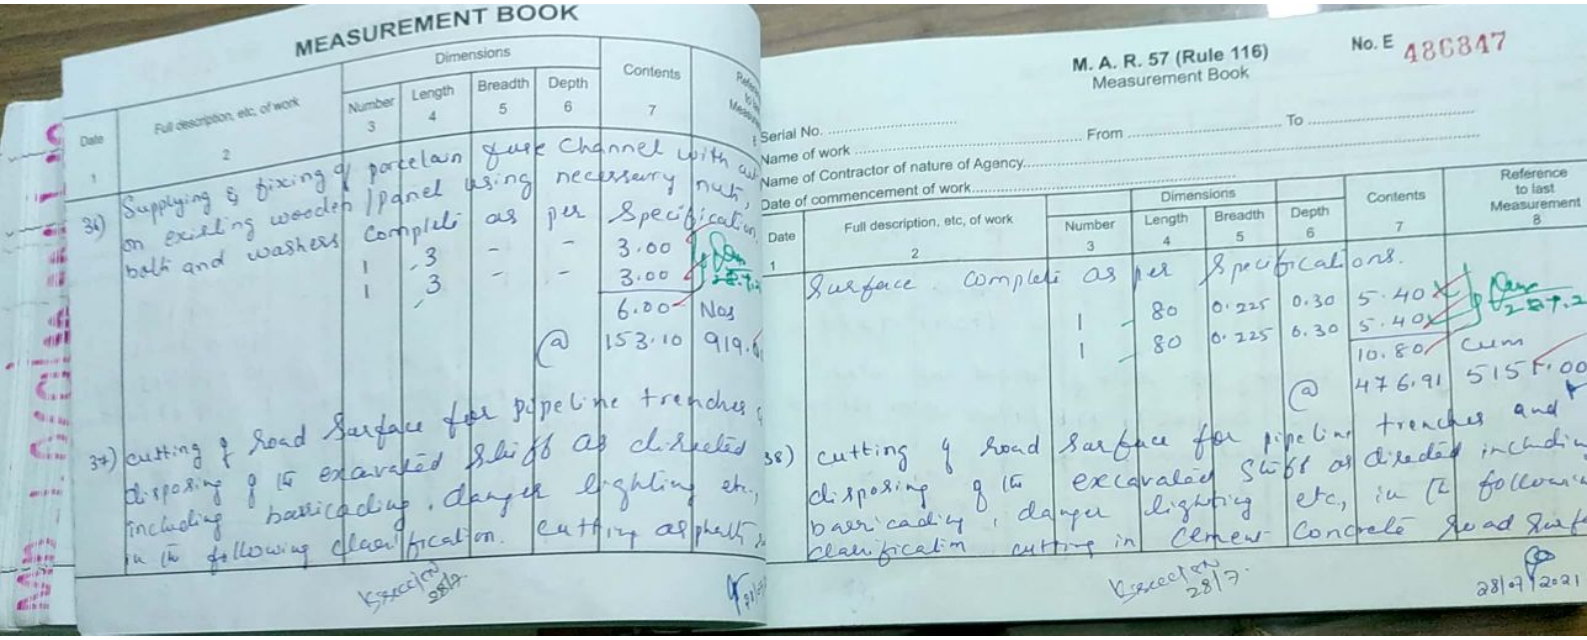

MEASUREMENT BOOK

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	
36)	Supplying & fixing of porcelain fuse Channel with cut on existing wooden panel using necessary nuts, bolts and washers Complete as per Specification	1	3	-	-	3.00	
		1	3	-	-	3.00	
						6.00	Nos
					@	153.10	919.6
37)	cutting & Road Surface for pipeline trenches disposing of the excavated Stuff as directed including barricading, danger lighting etc, in the following classification. cutting asphalt						

Execution 28/7

M. A. R. 57 (Rule 116)
Measurement Book

No. E 486847

Serial No. ..... From ..... To .....
Name of work .....
Name of Contractor of nature of Agency.....
Date of commencement of work.....

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	Surface Complete as per Specifications.	1	80	0.225	0.30	5.40	
		1	80	0.225	0.30	5.40	
						10.80	Cum
					@	476.91	5151.00
38)	cutting & Road Surface for pipeline trenches and disposing of the excavated Stuff as directed including barricading, danger lighting etc, in the following classification cutting in Cement Concrete Road Surface						

Execution 28/7

28/7/2021

Scanned by CamScanner

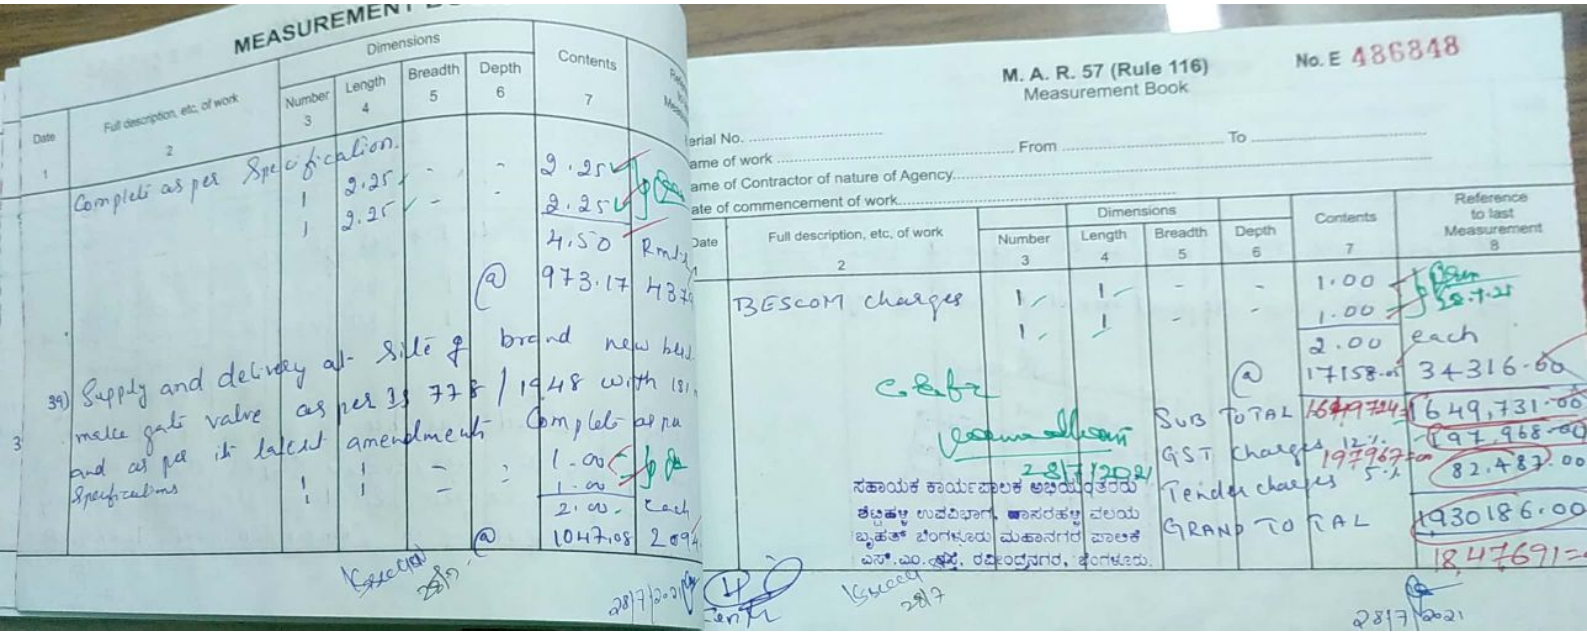

MEASUREMENT

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	Complete as per Specification.	1	2.25	-	-	2.25	
		1	2.25	-	-	2.25	
						4.50 Rmtr	
					@	973.17 4378	
39)	Supply and delivery at Site of brand new heavy melee gate valve as per IS 778 / 1948 with IS1 and as per its latest amendment Complete as per Specifications	1	1	-	-	1.00	
		1	1	-	-	1.00	
						2.00 Each	
					@	1047.08 2094	

Executed
28/7/2021

M. A. R. 57 (Rule 116)
Measurement Book

No. E 486848

Serial No. ..... From ..... To .....
Name of work .....
Name of Contractor of nature of Agency.....
Date of commencement of work.....

Date	Full description, etc, of work	Dimensions: Number	Length	Breadth	Depth	Contents	Reference to last Measurement
1	2	3	4	5	6	7	8
	BESCOM charges	1	1	-	-	1.00	
		1	1	-	-	1.00	
						2.00	each
					@	17158.00	34316.00
					SUB TOTAL	1649731	1649731.00
					GST charges 12%	197967	197968.00
					Tender charges 5%		82487.00
					GRAND TOTAL		1930186.00
							1847691

C.&Fr

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಕೆಟ್ಟಿಹಳ್ಳಿ ಉಪವಿಭಾಗ, ಚಾಸರಹಳ್ಳಿ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಎಸ್.ಎಂ.ಕೃಷ್ಣ, ರವೀಂದ್ರನಗರ, ಬೆಂಗಳೂರು.

28/7/2021

Executed
28/7

28/7/2021

Scanned by CamScanner

MEASURE

Date	Full description, etc. of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8

Certificate :

1) Certified that the work done is Satisfactory

2) There is no depart-mental issued by BBMP

Received
AE
28/7/21

28.7.21

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
'ಕೆಬ್ಬಹಳ್ಳಿ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
'ಎಸ್ ಎಂ. ರಸ್ತೆ, ಪದ್ಮನಾಭನಗರ, ಬೆಂಗಳೂರು

Audited and admitted for Rs. 847691-00
Passed by Chargeable for Rs. 177589-00

M. A. R. 57 (Rule 116)
Measurement Book

No. E 486849

Sanction No. Seventeen Lakhs Seventy Five Thousand Eight hundred and ninty Five only
Name of work 17795-00 From To
Name of Contractor of nature of Agency
Date of commencement of work

Date	Full description, etc. of work	Dimensions				Contents	Reference to last Measurement
		Number	Length	Breadth	Depth		
1	2	3	4	5	6	7	8

Received
AE
28/7/21

ಸಹಾಯಕ ಕಾರ್ಯಪಾಲಕ ಅಭಿಯಂತರರು
ಕೆಬ್ಬಹಳ್ಳಿ ಉಪವಿಭಾಗ, ದಾಸರಹಳ್ಳಿ ವಲಯ
ಬೃಹತ್ ಬೆಂಗಳೂರು ಮಹಾನಗರ ಪಾಲಿಕೆ
ಪದ್ಮನಾಭನಗರ, ಬೆಂಗಳೂರು

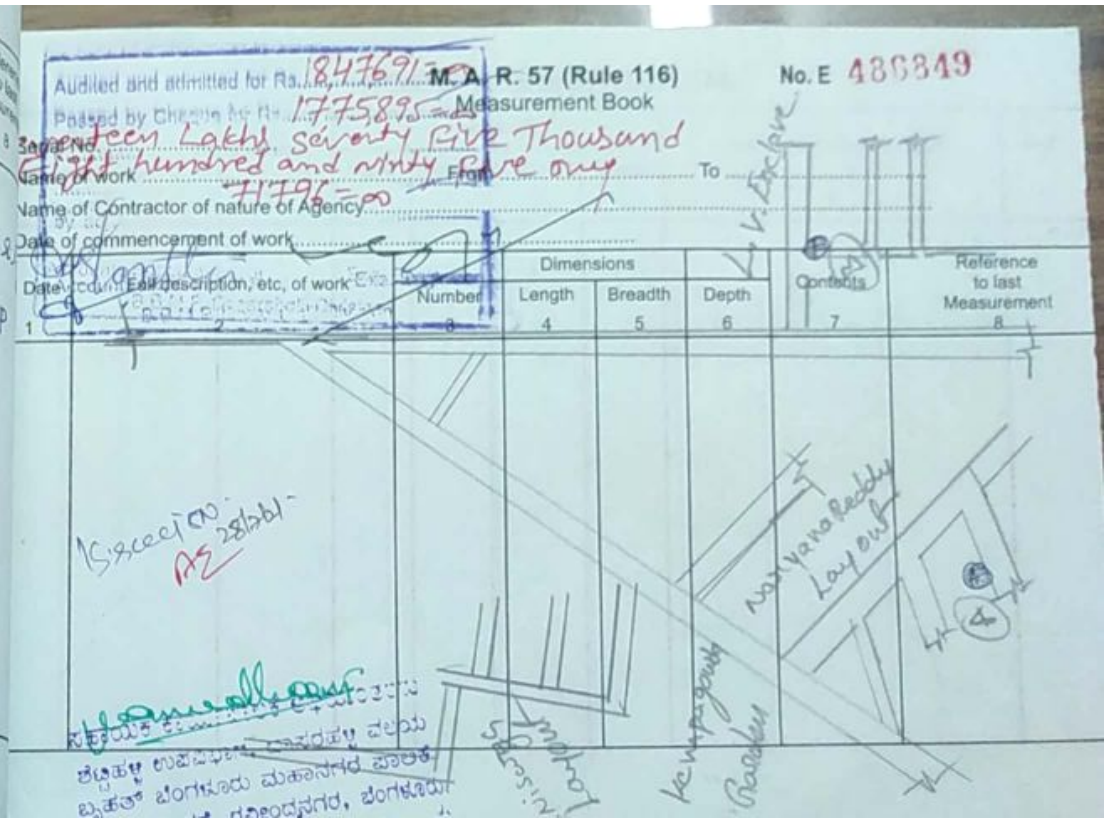

Scanned by CamScanner
